

King Street Tile Drain Inspections

Inspection Report for Observation:
Barrier1

Observation Location:

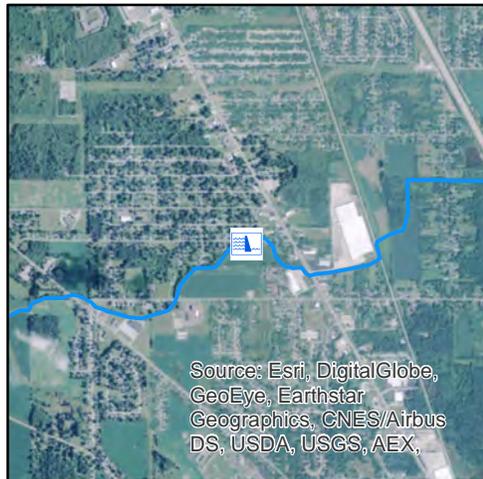


Photo 1



Material: Riprap

Length (feet): 25

Photo 1 Direction: Facing Upstream

Photo 2 Direction: Facing Downstream

Comments:

On south side of Kansas st crossing. Could be intentional as a flow control device. 25 ft long. Water is dammed up behind it into culvert. Rip rap as well as two pieces of curb.

Photo 2



CLIENT	Saginaw County Public Works Commissioner	 HUBBELL, ROTH & CLARK, INC CONSULTING ENGINEERS SINCE 1915	555 Hulet Drive P.O. Box 824 Bloomfield Hills, MI 48303-0824 (248) 454-6300 http://www.hrc-engr.com	DATE:	08/16/2016
				SCALE:	
NOTE				SHEET #:	
				JOB #:	20160331
